

ASSIGNMENT 4

- PM Solution -

MARASIGAN, VEM AIENSI A.
3BSCS-I

March 4, 2024

New Customer Onboarding Feature for G-Cash

As the project manager for developing a new customer onboarding feature, below are the task assignments for each role as well as how it will be executed.

Task Designation to Team Members

Task	Duration	Responsible
Gathering Requirements	1 week	Business Analyst
Design App View Layout	1 week + 2 days (7 days)	UI/UX Designer
Implement Layout	3 weeks	Front-end Dev
Integrate G-Cash Pay	3 weeks	Back-end Dev
Unit & Integration Testing	4 weeks	QA Tester
Deployment	3 days	Project Manager

The feature will undergo development for 8 weeks, a total of 40 days, excluding Sundays and Saturdays.

Gathering requirements: It involves gathering information regarding the needs of the user on how to interact with the new system, user stories, as well as the requirements for the team to implement gathered user stories. This also ends in a completion milestone where all team members are involved.

Design App View Layout: Contains how customer information is displayed within the system. For example, their current balance, payment buttons, and transaction history.

Implement Layout: The phase of creating code from the UI/UX design to make interaction possible. Building starts whenever an initial design layout is available.


Integrate G-Cash Pay: The phase of creating code that will enable G-Cash integration into the system. Building starts once functional buttons are created.

Unit & Integration Testing: Testing is conducted before completion of the Layout implementation as well as the G-Cash Pay Integration.

As for details, here are predecessors:

- | | |
|-------------------------------|---|
| 1. Design App View Layout | Starts after Completion of requirements gathering. |
| 2. Implement Layout | Starts after 3 days completion of Design View Layout. |
| 3. Integrate G-Cash Pay | Starts after 20% completion of Implement Layout. |
| 4. Unit & Integration Testing | Starts before 2 weeks completion of Implement Layout and Integrate G-Cash Pay |
| 5. Deployment | Starts after a day Completion of Unit & Integration tests |

Feature Development for G-Cash Integration

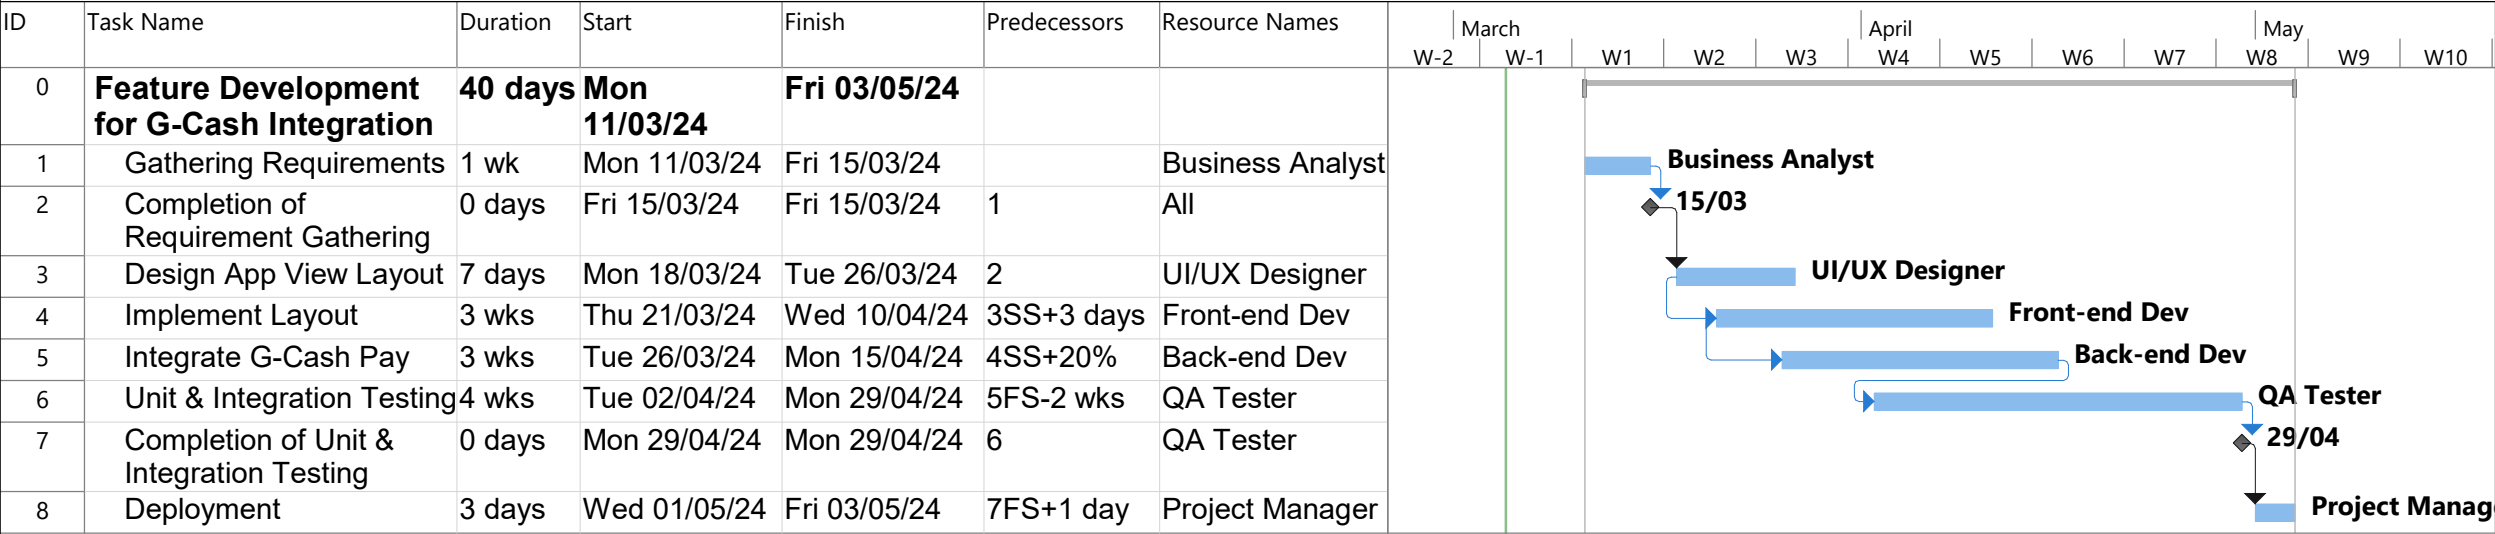

Project: Feature Development f
Date: Tue 05/03/24

Task		Inactive Task		Manual Summary Rollup		External Milestone	
Split		Inactive Milestone		Manual Summary		Deadline	
Milestone		Inactive Summary		Start-only		Progress	
Summary		Manual Task		Finish-only		Manual Progress	
Project Summary		Duration-only		External Tasks			
